

INCOR PBEL CITY PHASE 3 - CHENNAI

B6-Trinity:

Week-1



Footing reinforcement erection works in progress footing PCC Sludge removing work



Footing reinforcement erection works in progress, sludge cleaning for PCC in progress.

C1-Newport:

Week-1



UG sump pump room and column shuttering supporting works in progress..



Column and shear wall shuttering supporting and alignment works in progress.

C2-Destin:

Week-1



Excavation works in progress

E1-Malta:

Week-1



Soil levelling and compaction works in progress..



Soil levelling and compaction works in progress

C2-Destin:

Week-2



Excavation and rock strata chipping
works in progress

E1-Malta:

Week-2



U G sump plinth beam shuttering works in progress

B6-Trinity:

Week-3:



Footing and column reinforcement
erection works in progress



Footing & Column reinforcement and shuttering
works in progress, Sludge cleaning for footing
PCC works in progress

C1-Newport:

Week-3:



U G sump pump and 13 column
concreting work in progress



Concrete poured area curing works in
progress

C1-Newport:

Week-3:



U G sump pump room and 13 column
concrete planned



Reinforcement rust removal coating
works in progress

E1-Malta:

Week-3:



Plinth beam shuttering works in progress



U G sump plinth beam shuttering works in progress

B5-Marbella:

Week-4:



column and U G sump wall shuttering
board making works in progress



UG Sump wall reinforcement works in
progress

B5-Marbella:

Week-4:



B5 & C1 soil compaction testing in progress



B5-UG Sump wall shuttering board making works and sump wall steel rust chemical coating works in progress

B6-Trinity:


Week-4:



Footing and column reinforcement and footing shuttering works in progress. slush cleaning for PCC preparation



Footing and column reinforcement and footing shuttering works in progress. slush cleaning for PCC

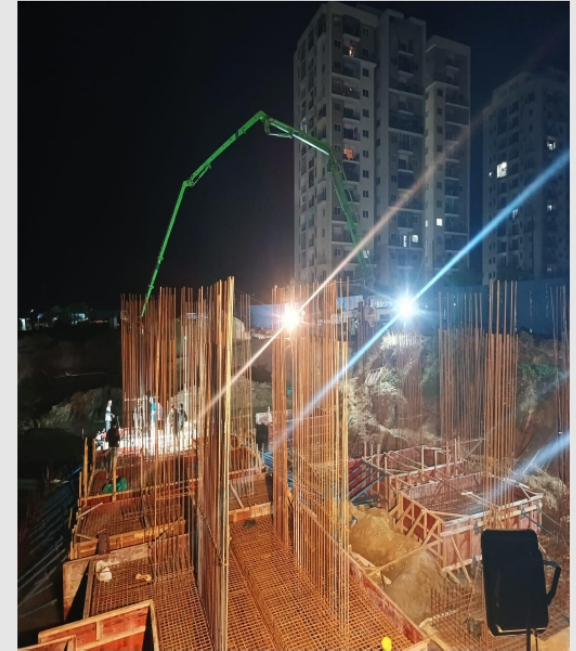

footing concrete pouring works started

B6-Trinity:

Week-4:



Footing PCC concrete 7cum planned today Footing RCC 90cum planned



Footing PCC works in progress



Footing concrete in progress

B6-Trinity:

Week-4:



54Cum footing concrete in progress



column and U G sump wall shuttering board making works in progress



Footing reinforcement and shuttering works in progress footing PCC Sludge cleaning works in progress

C1-Newport:

Week-4:



Curing works and deshuttering works in progress, north side final layer backfilling works in progress



2nd lift column shuttering board making works in progress



south side waterproofing coating preparation works

C1-Newport:

Week-4:



South side waterproofing coating preparation works in progress

C2-Destin:

Week-4:



Excavation work in progress
(Below 3M Depth)



Excavation work completed upto
4m depth, awaiting for consultant
formation

C3-Miramar:

Week-4:



Excavation work commenced



Excavation works in progress



Excavation works in progress

E1-Malta:

Week-4:



UG Sump plinth beam shuttering work is in progress



UG Sump plinth beam shuttering work is in progress. Waterproofing coating completed area protection sheet fixing works in progress

E1-Malta:

Week-4:



UG Sump plinth beam concrete planned



Sump plinth beam shuttering works
